

# **EXHIBIT B**

**From:** [Matthew Cecil](#)  
**To:** [Jackson, Larry](#)  
**Cc:** [Bharath Singh](#); [Ryan Deely](#)  
**Subject:** Tyson HT - Pad Ready Impact  
**Date:** Monday, March 25, 2019 4:48:20 PM  
**Attachments:** [image606178.png](#)  
[image724260.png](#)  
[image290344.png](#)  
[image193934.png](#)  
[image961443.png](#)  
[2019-0321-Gray-TRT-3r1-Overall.pdf](#)  
[Tyson HT - Pad Ready Impact Summary\\_03252019.pptx](#)

---


Hello Larry,


As we discussed, attached is the latest schedule reflecting a pad turnover from Tyson's separate contractor of 7/1/2019. Below are categories of cost and time impacts from this delayed pad turnover from Tyson's contractor to Gray, as well as the impact to the overall project time line. The attached schedule does not account for any additional schedule pushes, and any unforeseen or additional impacts will push the schedule day for day. Below, in general, describes the known impacts and the future "possible" impacts. Also attached is a summary sheet that describes the push visually.

- Known Impacts: Quantifiable:
  - Winter Work Will Occur. Additional cost and time impacts should be expected.
  - 4-4.5 Mos. of additional General Conditions cost Impacted as of now.
  - Building Dry In date extension.
  - Expected Billing percentages for Gray fiscal year ending 9/30/2019. Original projection 95%, current expected projection 25%.
  - Building turnover to Tyson extended.
  - Potential for Additional cost for storage of fabricated materials.
  - Subcontractor Pricing Increase i.e. Steel, PEMB etc.
- Future Possible impacts: Not Yet Quantifiable:
  - Schedule continued push due to pad ready.
  - Construction Activities Delayed Due to Tennessee Weather influence Window. Nov 1<sup>st</sup>, 2019 – March 30<sup>th</sup>, 2020
  - Availability of Subcontractors
  - Continued Subcontractor Pricing Increases
  - Tyson SOP date.
  - Increased Cohabitation and stacking of tradespeople w/ Tyson retained subs.  
Decreasing Productivity Factors for all. This will also heighten the need for increased safety monitoring/staffing for all parties.

Gray will endeavor to work collaboratively with Tyson to minimize the impacts associated with this delay but as you can gather from the attached documents, there are definite cost impacts that are starting to affect us and the project.

## Pad Ready Impact Summary

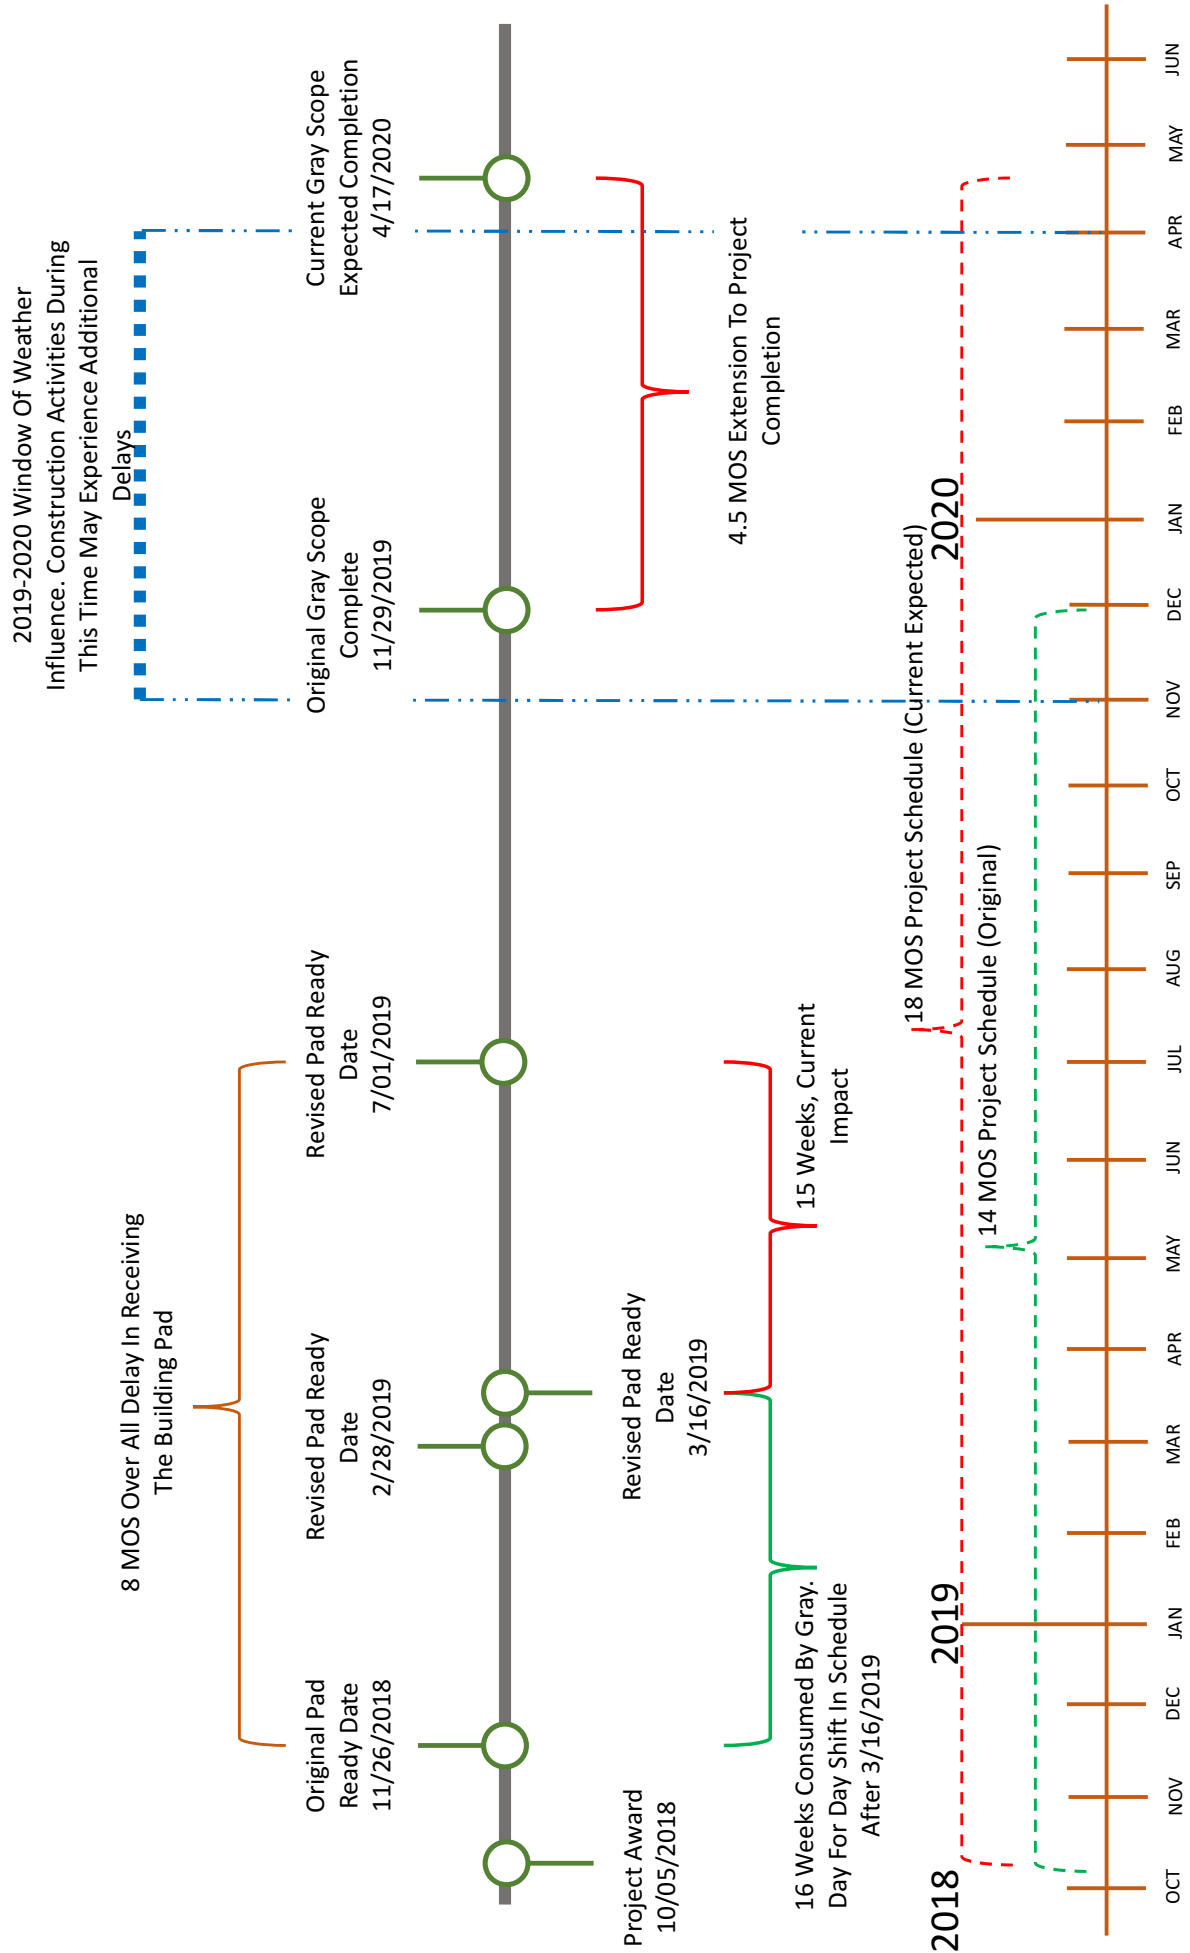

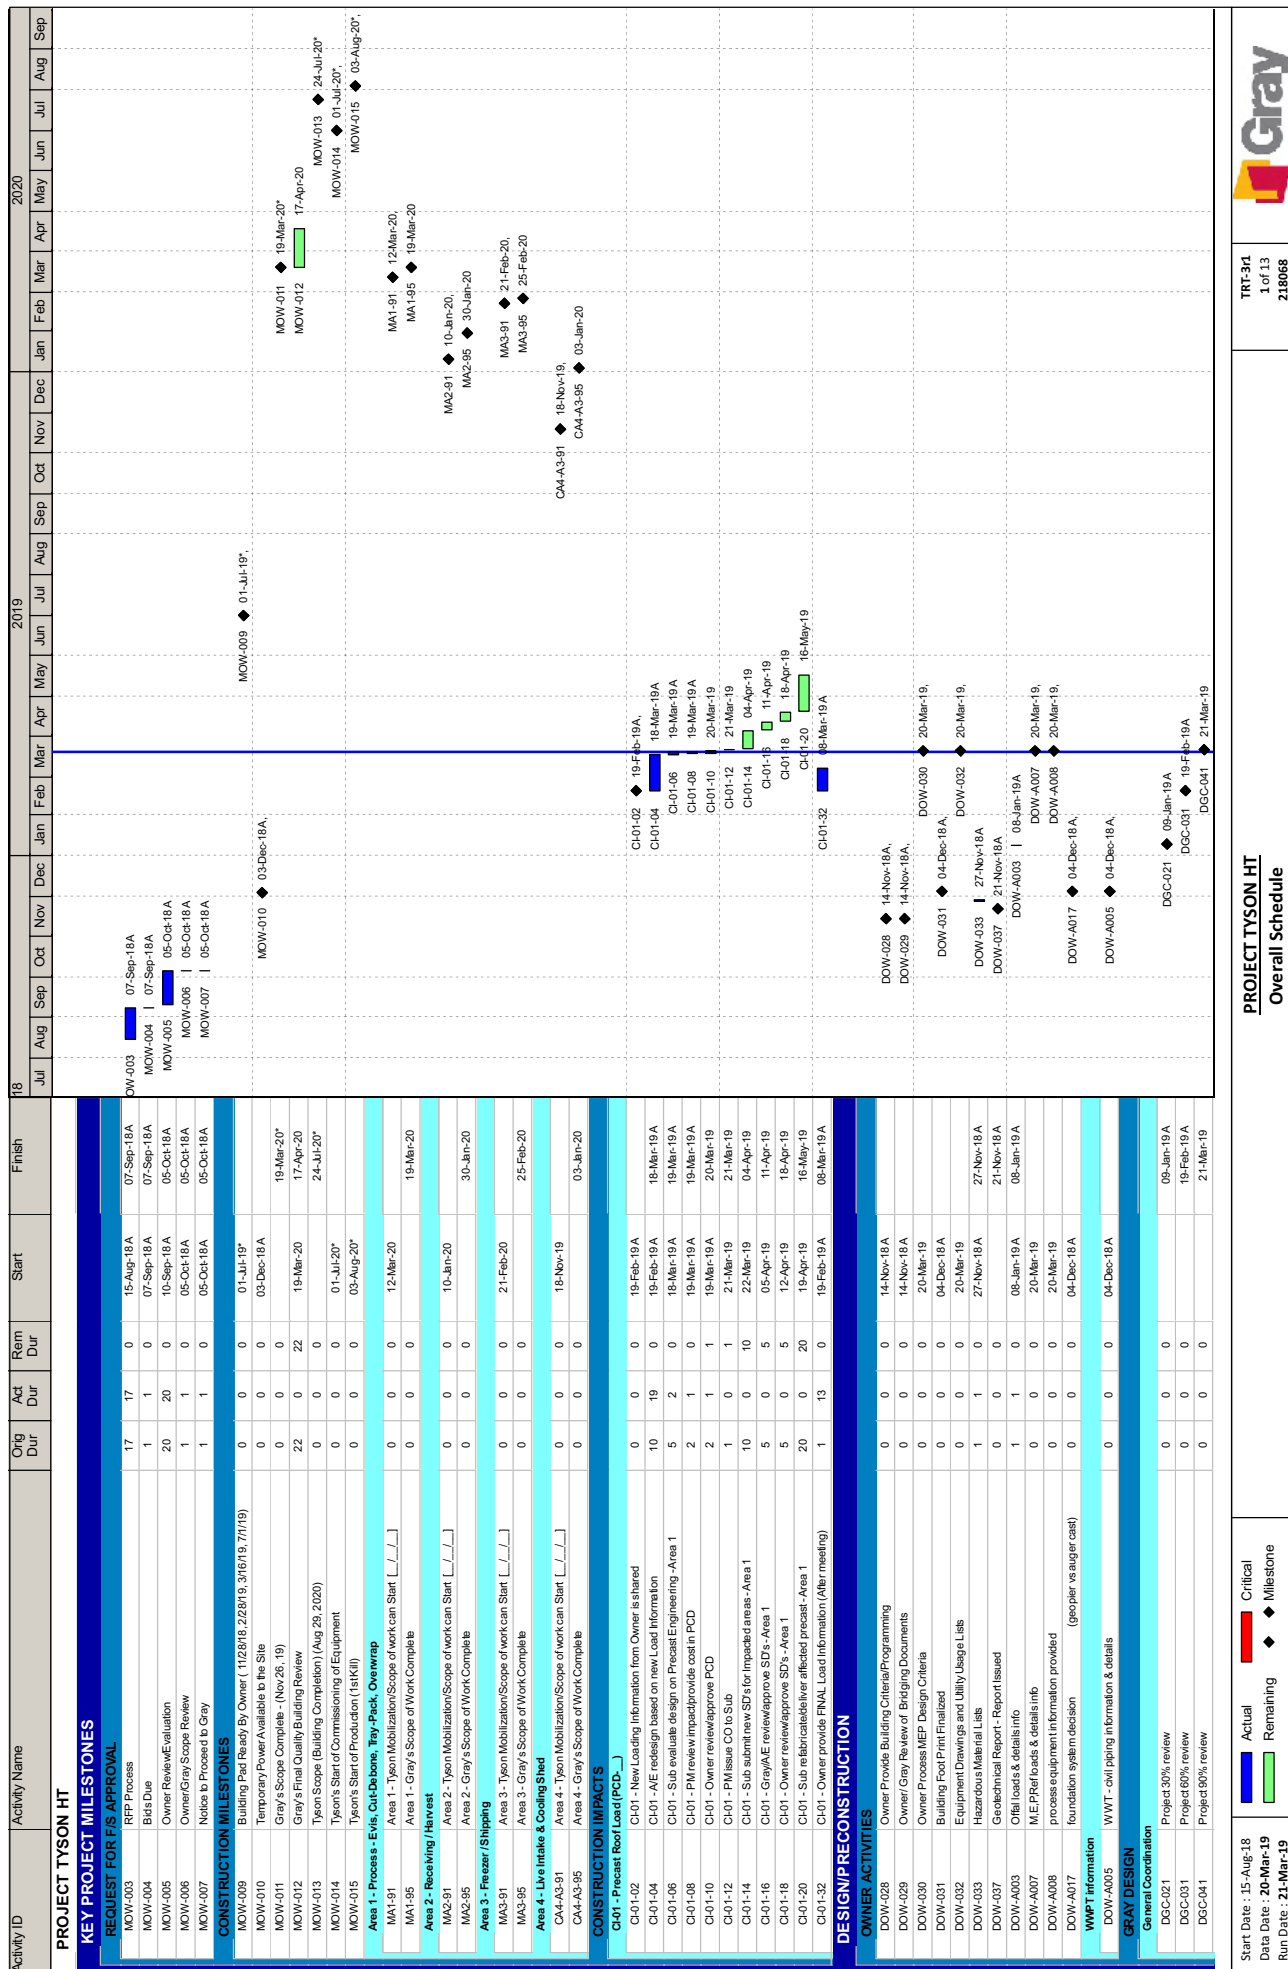


TRT-31  
1 of 13  
218068

PROJECT TYSON HT  
Overall Schedule

Actual  
Remaining  
Critical  
Milestone

Start Date : 15-Aug-18  
Data Date : 20-Mar-19  
Run Date : 21-Mar-19

Activity ID		Activity Name		Orig	Ast	Rem	Start	Finish	2018												2019												2020																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
				Dur	Dur	Dur			Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb

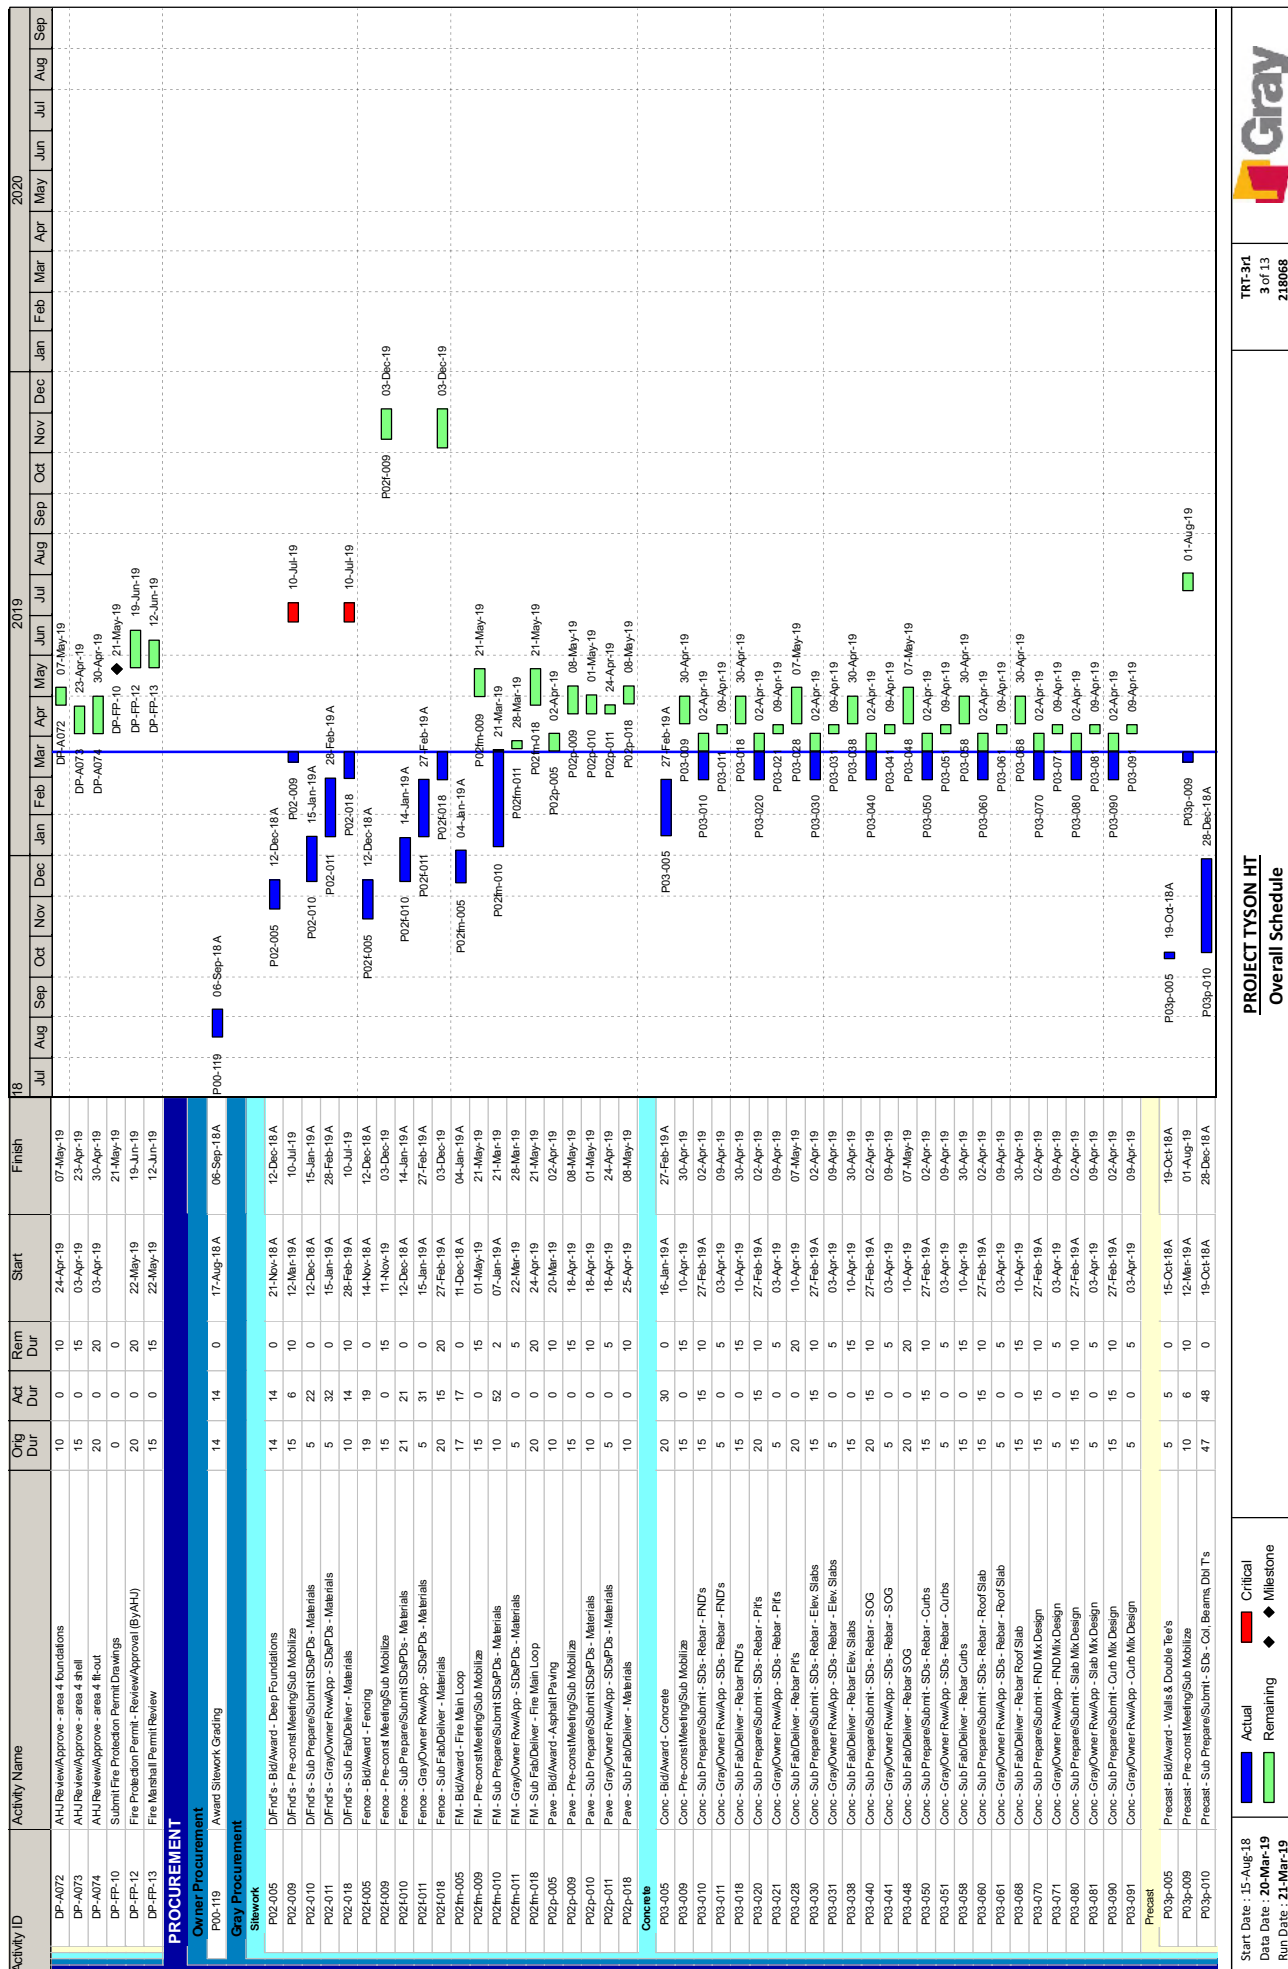

[illegible]

Activity ID		Activity Name	Orig Dur	Act Dur	Rem Dur	Start	Finish	2019												2020															
								Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	
P07c-005	Caulk - Bid/Award - Caulking	15	0	15	20-Mar-19	09-Apr-19																													
P07c-009	Caulk - Sub Prepare/Submit S/Ds/PDs - Materials	15	0	15	24-Apr-19	14-May-19																													
P07c-010	Caulk - Sub Prepare/Submit S/Ds/PDs - Materials	10	0	10	10-Apr-19	23-Apr-19																													
P07c-011	Caulk - Gray/Owner Rvw/App - SDs/PDs - Materials	5	0	5	24-Apr-19	30-Apr-19																													
P07c-018	Caulk - Sub Fab/Deliver - Materials	10	0	10	01-May-19	14-May-19																													
Siding																																			
P07i-005	IMP - Bid/Award - Insulated Metal Panels	20	33	7	01-Feb-19 A	28-Mar-19																													
P07i-009	IMP - Pre-const Meeting/Sub Mobilize	15	0	15	17-Jun-19	08-Jul-19																													
P07i-010	IMP - Sub Prepare/Submit S/Ds - A3 - IMP	15	0	15	29-Mar-19	18-Apr-19																													
P07i-011	IMP - Gray/Owner Rvw/App S/Ds - A3 - IMP	5	0	5	19-Apr-19	25-Apr-19																													
P07i-018	IMP - Sub Fab/Deliver - A3 - IMP	30	0	30	26-Apr-19	07-Jun-19																													
P07i-020	IMP - Sub Prepare/Submit S/Ds - A1 - IMP	10	0	10	19-Apr-19	02-May-19																													
P07i-021	IMP - Gray/Owner Rvw/App S/Ds - A1 - IMP	5	0	5	03-May-19	09-May-19																													
P07i-028	IMP - Sub Fab/Deliver - A1 - IMP	30	0	30	10-May-19	21-Jun-19																													
P07i-030	IMP - Sub Prepare/Submit S/Ds - A2/A4 - IMP	10	0	10	03-May-19	16-May-19																													
P07i-031	IMP - Gray/Owner Rvw/App S/Ds - A2/A4 - IMP	5	0	5	17-May-19	23-May-19																													
P07i-038	IMP - Sub Fab/Deliver - A2/A4 - IMP	30	0	30	24-May-19	08-Jul-19																													
Doors & Windows																																			
OH Doors																																			
P08-005	OHD - Bid/Award - Overhead Doors	15	43	7	18-Jun-19 A	28-Mar-19																													
P08-009	OHD - Pre-const Meeting/Sub Mobilize	15	0	15	03-May-19	23-May-19																													
P08-010	OHD - Sub Prepare/Submit S/Ds/PDs - ALL Types	15	0	15	29-Mar-19	18-Apr-19																													
P08-011	OHD - Gray/Owner Rvw/App - SDs/PDs - ALL Types	5	0	5	19-Apr-19	25-Apr-19																													
P08-018	OHD - Sub Fab/Deliver - ALL Types	20	0	20	26-Apr-19	02-May-19																													
Mandors																																			
P08m-005	MID - Bid/Award - Mandors	15	43	7	18-Jun-19 A	23-Apr-19																													
P08m-009	MID - Pre-const Meeting/Sub Mobilize	15	0	15	30-May-19	19-Jun-19																													
P08m-010	MID - Sub Prepare/Submit S/Ds - CMJ & Pre-Cast Frames	15	0	15	03-Apr-19	23-Apr-19																													
P08m-011	MID - Gray/Owner Rvw/App - S/Ds - CMJ & Pre-Cast Frames	5	0	5	24-Apr-19	30-Apr-19																													
P08m-018	MID - Sub Fab/Deliver - CMJ & Pre-Cast Frames	15	0	15	01-May-19	21-May-19																													
P08m-020	MID - Sub Prepare/Submit S/Ds - Remain Frames/Door slabs	10	0	10	24-Apr-19	07-May-19																													
P08m-021	MID - Gray/Owner Rvw/App - S/Ds - Remain Frames/Door slabs	5	0	5	08-May-19	14-May-19																													
P08m-028	MID - Sub Fab/Deliver - Remain Frames/Door slabs	30	0	30	15-May-19	26-Jun-19																													
P08m-030	MID - Sub Prepare/Submit - PDs - Door Hardware	20	0	20	03-Apr-19	30-Apr-19																													
P08m-031	MID - Gray/Owner Rvw/App - PDs - Door Hardware	5	0	5	01-May-19	07-May-19																													
P08m-038	MID - Sub Fab/Deliver - Door Hardware	30	0	30	08-May-19	19-Jun-19																													
Finishes																																			
P09-005	Paint - Bid/Award - Interior Painting	20	0	20	09-May-19	06-Jun-19																													
P09-009	Paint - Pre-const Meeting/Sub Mobilize	15	0	15	08-Jul-19	26-Jul-19																													
P09-010	Paint - Sub Prepare/Submit - PDs/Samples - Materials	15	0	15	07-Jun-19	27-Jun-19																													
P09-011	Paint - Gray/Owner Rvw/App - PDs/Samples - Materials	5	0	5	28-Jun-19	05-Jul-19																													
P09-018	Paint - Sub Fab/Deliver - Materials	15	0	15	08-Jul-19	26-Jul-19																													
Specialties																																			
P10-005	Spec - Bid/Award - Specialties	20	43	10	18-Jan-19 A	20-Jun-19																													
P10-009	Spec - Pre-const Meeting/Sub Mobilize	15	0	15	19-Aug-19	09-Sep-19																													
P10-010	Spec - Sub Prepare/Submit - S/Ds/PDs - Materials	20	0	20	21-Jun-19	19-Jul-19																													
P10-011	Spec - Gray/Owner Rvw/App - SDs/PDs - Materials	5	0	5	22-Jul-19	26-Jul-19																													
P10-018	Spec - Sub Fab/Deliver - Materials	30	0	30	29-Jun-19	09-Sep-19																													
Dock Equipment																																			
P11-005	Dock - Bid/Award - Dock Equipment	15	43	4	18-Jan-19 A	02-Apr-19																													
P11-009	Dock - Pre-const Meeting/Sub Mobilize	15	0	15	06-Jun-19	26-Jun-19																													
P11-010	Dock - Sub Prepare/Submit - S/Ds/PDs - Materials	15	0	15	03-Apr-19	23-Apr-19																													
P11-011	Dock - Gray/Owner Rvw/App - SDs/PDs - Materials	5	0	5	24-Apr-19	30-Apr-19																													
P11-018	Dock - Sub Fab/Deliver - Materials	40	0	40	01-May-19	26-Jun-19																													
Truck Scales																																			
P12-005	TS - Bid/Award - Truck Scales	20	20	0	06-Dec-18 A	04-Jan-19 A																													
P12-009	TS - Pre-const Meeting/Sub Mobilize	15	0	15	27-Jan-19	17-May-19																													
P12-010	TS - Sub Prepare/Submit - SDs/PDs - Materials (#2)	15	49	0	07-Jan-19 A	15-Mar-19 A																													
P12-011	TS - Gray/Owner Rvw/App - S/Ds/PDs - Materials (#2)	5	30	3	06-Feb-19 A	22-Mar-19																													
P12-018	TS - Sub Fab/Deliver - Materials	40	0	40	25-Mar-19	17-May-19																													
Pre-engineered Buildings																																			
P13-005	PEB - Bid/Award - PEB Buildings	30	37	0	06-Dec-18 A	30-Jan-19 A																													
P13-009	PEB - Pre-const Meeting/Sub Mobilize	15	0	15	13-Jun-19	03-Jul-19																													



**PROJECT TYSON HT**  
**Overall Schedule**

**PROJECT TYSON HT**  
**Overall Schedule**



Activity ID	Activity Name	Orig Dur	Act Dur	Rem Dur	Start	Finish	2018												2019												2020											
							Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep									
CA2-0288	A2 - Pit - Backfill Pit (If Req'd, as no sheet piles)	5	0	5	19-Sep-19	25-Sep-19																																				
CA2-0301	A2 - Install Girders	8	0	8	11-Jul-19	25-Jul-19																																				
CA2-0310	A2 - EFRen+P RND Cap+Grade Beams - ALL AREAS	8	0	8	16-Jul-19	25-Jul-19																																				
CA2-0342	A2 - Pft - MuorRP Pft Slab & FND @ 77' 6 and 82.6)	12	0	12	08-Aug-19	23-Aug-19																																				
CA2-0346	A2 - Pft - FRP Pft Walls - All 4 sides	15	0	15	16-Aug-19	06-Sep-19																																				
CA2-0508	A2 - Pft - Install Handrails around Pft	4	0	4	09-Sep-19	12-Sep-19																																				
CA2-0708	A2 - Pft - Install Waterproofing	8	0	8	09-Sep-19	18-Sep-19																																				
CA2-9010	A2 - EOR Letter - RND Readyfor Precast Install - ALL AREAS	0	0	0	01-Aug-19	01-Aug-19																																				
Structure																																										
CA2-0320	A2 - Erect Precast (Wale&BeamTie's) - ALL AREAS	12	0	12	26-Sep-19	14-Oct-19																																				
CA2-0320x	A2 - Remove Precast Bracing - ALL AREAS	3	0	3	21-Oct-19	23-Oct-19																																				
CA2-0360	A2 - Grout Precast - ALL AREAS	14	0	14	27-Sep-19	17-Oct-19																																				
CA2-0541	A2 - Install Wall Framing - Col H	5	0	5	24-Oct-19	30-Oct-19																																				
CA2-9050	A2 - Testing Inspect - Precast Readyfor Brace Removal - ALL	1	0	1	18-Oct-19	18-Oct-19																																				
Concrete Slabs																																										
CA2-0360a	A2 - Excavate & Set Trench Rebar - ALL AREAS	10	0	10	14-Nov-19	27-Nov-19																																				
CA2-0360b	A2 - Place mud mat & Set precast Silt trench - ALL AREAS	10	0	10	19-Nov-19	04-Dec-19																																				
CA2-0360c	A2 - EFRFP FND for CMU walls - ALL AREAS	4	0	4	14-Nov-19	19-Nov-19																																				
CA2-0370a	A2 - Place final subgrade materials - ALL AREAS	6	0	6	22-Nov-19	27-Nov-19																																				
CA2-0370b	A2 - VIRFP Concrete slab (4 pour)	15	0	15	20-Nov-19	16-Dec-19																																				
CA2-0390	A2 - RFP Concrete Cuts - ALL AREAS	16	0	16	17-Dec-19	09-Jan-20																																				
CA2-2220	A2 - UG Sanitary Piping	5	0	5	24-Oct-19	30-Oct-19																																				
CA2-2420	A2 - UG Process Waste Piping	15	0	15	24-Oct-19	13-Nov-19																																				
Building Enclosure																																										
CA2-0380	A2 - FIRE+P Roof Epping Slab - ALL AREAS	6	0	6	25-Oct-19	01-Nov-19																																				
CA2-0560	A2 - Install RTU Platforms	15	0	15	01-Nov-19	21-Nov-19																																				
CA2-0710	A2 - Install Roofing System - ALL AREAS	12	0	12	01-Nov-19	18-Nov-19																																				
CA2-0721	A2 - Install MP System - Col H	4	0	4	31-Oct-19	05-Nov-19																																				
CA2-0790	A2 - Install Precast Guiding - ALL AREAS	9	0	9	24-Oct-19	05-Nov-19																																				
CA2-0810	A2 - Install OH/Dock Equipment	5	0	5	17-Dec-19	23-Dec-19																																				
CA2-0860	A2 - Install Frame/Door/Hardware - Exterior Doors (ALL)	5	0	5	17-Dec-19	23-Dec-19																																				
Finishes																																										
CA2-0417	A2 - Install CMU - Separation Walls	12	0	12	20-Nov-19	09-Dec-19																																				
CA2-0733	A2 - Install MP walls - ALL AREAS	8	0	8	17-Dec-19	27-Dec-19																																				
CA2-0743	A2 - Install Caulking/Sealing @ IMP on Col M	8	0	8	30-Dec-19	09-Jan-20																																				
CA2-0820	A2 - Install Interior OH Doors - ALL	10	0	10	30-Dec-19	13-Jan-20																																				
CA2-0870	A2 - Install Frame/Door/Hardware - Interior Doors (ALL)	8	0	8	30-Dec-19	09-Jan-20																																				
CA2-0917	A2 - Install MI Studs - Separation Walls	8	0	8	17-Dec-19	27-Dec-19																																				
CA2-0927	A2 - Install Gyp Bd (Hanging/Finish) - Separation Walls in Col M-V+15(A)	12	0	16	30-Dec-19	21-Jan-20																																				
CA2-0960	A2 - Final Paint - (All Items) - All Areas	16	0	12	14-Jan-20	29-Jan-20																																				
Electrical																																										
CA2-2670	A2 - RUPull Wire/Term - Fire Alarm Wiring/Devices	15	0	15	17-Dec-19	08-Jan-20																																				
Fire Protection																																										
CA2-2130	A2 - Install FP Main/Branches - ALL AREAS	12	0	12	17-Oct-19	01-Nov-19																																				
CA2-2180	A2 - Stack FP Main Risers	4	0	4	17-Dec-19	20-Dec-19																																				
CA2-2190	A2 - Install FP Below Mech/Elec Obstructions - ALL Areas (POST-Tycon)	10	0	10	01-Jan-20	12-Jan-20																																				
Support Areas																																										
CA2-0999	A2 - Finishes and Supporting Areas	60	0	60	16-Sep-19	11-Dec-19																																				
TO BE RWID - RESTROOMS																																										
CA2-8006	PL RFR - Install CMU Above Slab	5	0	5	17-Dec-19	21-Dec-19																																				
CA2-8008	PL RFR - Install Steel Support Deck	2	0	2	22-Dec-19	23-Dec-19																																				
CA2-8010	PL RFR - Block Filler/Prime Paint CMU	3	0	3	22-Dec-19	23-Dec-19																																				
CA2-8012	PL RFR - FRP Slab on Dock	4	0	4	24-Dec-19	27-Dec-19																																				
CA2-8016	PL RFR - Hang/install EF/Durwork (- NIC -)	3	0	3	28-Dec-19	30-Dec-19																																				
CA2-8018	PL RFR - Drops & RUF Piping	2	0	2	28-Dec-19	29-Dec-19																																				
CA2-8020	PL RFR - R/Elec conduit (ALL) (- NIC -)	5	0	5	28-Dec-19	01-Jan-20																																				
CA2-8021	PL RFR - Install OH Doors	5	0	5	26-Dec-19	02-Jan-20																																				
CA2-8028	PL RFR - Pull Wire/Set Devices - Mech Conv OH Doors (- NIC -)	3	0	3	31-Dec-19	02-Jan-20																																				
CA2-8030	PL RFR - Pull Wire - Fixtures - Lights (- NIC -)	3	0	3	29-Dec-19	31-Dec-19																																				
CA2-8032	PL RFR - Pull Wire/Set Devices - Fire Alarm	2	0	2	29-Dec-19	30-Dec-19																																				
CA2-8034	PL RFR - R/VA/G Plumbing (- NIC -)	3	0	3	31-Dec-19	02-Jan-20																																				
CA2-8036	PL RFR - Install/ACT Grid	2	0	2	03-Jan-20	04-Jan-20																																				

Start Date : 15-Aug-18

Data Date : 20-Mar-19

Run Date : 21-Mar-19

Actual

Remaining

Critical

Milestone

PROJECT TYSON HT

Overall Schedule

TRT-3r1


9 of 13

218068

Activity ID	Activity Name	Orig Dur	Act Dur	Rem Dur	Start	Finish	2018												2019												2020																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															
							Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													
CA2-8038	PL RRR - Install Diffusers/Gills in ACT (- NIC -)	2	0	2	05-Jan-20	06-Jan-20																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								</

Activity ID	Activity Name	Orig Dur	Act Dur	Rem Dur	Start	Finish	2019												2020																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
							Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													
CA3-0595	A3 - Install Roof/Mezz Deck - Office	2	0	2	20-Sep-19	23-Sep-19																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								

Activity ID	Activity Name	Orig Dur	Act Dur	Rem Dur	Start	Finish	2019												2020											
							Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun
CA3-0796	A3 - Install Precast Caulking - Utility	8	0	8	04-Sep-19	13-Sep-19																								
CA3-0810	A3 - Install Interior OHD -ALL AREAS	18	0	18	11-Nov-19	06-Dec-19																								
CA3-0860	A3 - Install Frame/Door Hardware - Exterior Doors (ALL)	15	0	15	09-Dec-19	30-Dec-19																								
CA3-1110	A3 - Install Dock Equipment -ALL AREAS	12	0	12	19-Nov-19	06-Dec-19																								
CA3-2377	A3 - Install Louvers - Utility	5	0	5	20-Aug-19	26-Aug-19																								
Finishes																														
CA3-0411	A3 - Install CMU - Dwg, Electrical Room	18	0	18	09-Dec-19	03-Jan-20																								
CA3-0415	A3 - Install CMU - Office	18	0	18	30-Jan-20	24-Feb-20																								
CA3-0416	A3 - Install CMU - Utility, Mech Room	18	0	18	06-Jan-20	29-Jan-20																								
CA3-0731	A3 - Install Interior IMP walls - Separation Walls - Dwg Blast/Supporting	10	0	10	22-Nov-19	31-Oct-19																								
CA3-0733	A3 - Install Interior IMP walls (RND) - WPC, South Wall	8	0	8	22-Oct-19	09-Dec-19																								
CA3-0734	A3 - Install Interior IMP walls (RND) - Dock	4	0	4	31-Oct-19	05-Nov-19																								
CA3-0737	A3 - Install IMP walls - Separation Walls - Cor P15-32	6	0	6	06-Nov-19	13-Nov-19																								
CA3-0738	A3 - Install IMP walls - Separation Walls - Cor V15-32	6	0	6	14-Nov-19	21-Nov-19																								
CA3-0741	A3 - Install Caulking/Sealing @ IMP - Walls/Ceilings - Dwg Blast/Support	12	0	12	10-Dec-19	26-Dec-19																								
CA3-0743	A3 - Install Caulking/Sealing @ IMP - WPC, South Wall	12	0	12	01-Nov-19	18-Nov-19																								
CA3-0744	A3 - Install Caulking/Sealing @ IMP - Dock	6	0	6	06-Nov-19	13-Nov-19																								
CA3-0747	A3 - Install Caulking/Sealing @ IMP - Separation Walls - Cor P15-32	6	0	6	14-Nov-19	21-Nov-19																								
CA3-0748	A3 - Install Caulking/Sealing @ IMP - Separation Walls - Cor V15-32	6	0	6	22-Nov-19	03-Dec-19																								
CA3-0751	A3 - Install IMP Ceiling - Dwg Blast	15	0	15	14-Nov-19	06-Dec-19																								
CA3-0820	A3 - Install Interior OH Doors - ALL AREAS	20	0	20	08-Nov-19	09-Dec-19																								
CA3-0870	A3 - Install Frame/Door Hardware - Interior Doors -ALL AREAS	20	0	20	22-Nov-19	23-Dec-19																								
CA3-0960	A3 - Final Paint - (All Items) -ALL AREAS	20	0	20	31-Dec-19	28-Jan-20																								
Electrical																														
CA3-2670	A3 - RUPull Wire/Form - Fire Alarm Wiring Devices	50	0	50	05-Dec-19	14-Feb-20																								
Fire Protection																														
CA3-2130	A3 - Install FPF Main/Brandsides -ALL AREAS	20	0	20	09-Oct-19	05-Nov-19																								
CA3-2180	A3 - Stack FPF Main Risers	12	0	12	22-Nov-19	11-Dec-19																								
CA3-2190	A3 - Install FPF Below Mech/Elec Obstructions -ALL Areas (POST-Tyson)	20	0	20	29-Jan-20	27-Jul-20																								
TO BE RWMD - -- RESTROOMS																														
CA3-8006	PL RRR - Install CMU Above Slab	5	0	5	17-Dec-19	23-Dec-19																								
CA3-8008	PL RRR - Install Steel Support/Dock	2	0	2	22-Dec-19	23-Dec-19																								
CA3-8010	PL RRR - Block Filler/Prime Paint CMU	3	0	3	22-Dec-19	24-Dec-19																								
CA3-8012	PL RRR - RRP Slab on Deck	3	0	3	24-Dec-19	27-Dec-19																								
CA3-8016	PL RRR - Hanger/Initial EF Ductwork (- NIC -)	4	0	4	28-Dec-19	30-Dec-19																								
CA3-8018	PL RRR - Drops & R/P FPF Piping	2	0	2	28-Dec-19	29-Dec-19																								
CA3-8020	PL RRR - R/P (elec conduit (ALL)) (- NIC -)	5	0	5	28-Dec-19	01-Jan-20																								
CA3-8021	PL RRR - Install OH Doors	5	0	5	26-Dec-19	02-Jan-20																								
CA3-8028	PL RRR - Pull Wire/Set Devices - Mech, Conv OH Doors (- NIC -)	3	0	3	31-Dec-19	02-Jan-20																								
CA3-8030	PL RRR - Pull Wire - Features - Lights (- NIC -)	3	0	3	29-Dec-19	31-Dec-19																								
CA3-8032	PL RRR - Pull Wire/Set Devices - Fire Alarm	2	0	2	29-Dec-19	30-Dec-19																								
CA3-8034	PL RRR - R/IAAG Plumbing (- NIC -)	3	0	3	31-Dec-19	02-Jan-20																								
CA3-8036	PL RRR - Install IA/ACT Grid	2	0	2	03-Jan-20	04-Jan-20																								
CA3-8038	PL RRR - Install Diffusers/Grills in ACT (- NIC -)	2	0	2	05-Jan-20	06-Jan-20																								
CA3-8040	PL RRR - Install Lights in ACT (- NIC -)	2	0	2	05-Jan-20	06-Jan-20																								
CA3-8042	PL RRR - Install FPF Heads in ACT	2	0	2	05-Jan-20	06-Jan-20																								
CA3-8044	PL RRR - Install IA/ACT Tiles	3	0	3	05-Jan-20	07-Jan-20																								
CA3-8046	PL RRR - Finish Paint	2	0	2	08-Jan-20	09-Jan-20																								
CA3-8048	PL RRR - Install Epoxy	2	0	2	10-Jan-20	11-Jan-20																								
CA3-8050	PL RRR - Install Diffusers & Shower Units (- NIC -)	4	0	4	12-Jan-20	13-Jan-20																								
CA3-8052	PL RRR - Install Mandrels & Hardware	2	0	2	12-Jan-20	13-Jan-20																								
CA3-8054	PL RRR - Set Bolt Partitions and Accessories	3	0	3	13-Jan-20	15-Jan-20																								
CA3-8058	PL RRR - Ceramic Tile	4	0	4	08-Jan-20	11-Jan-20																								
CA3-8099	PL RRR - AREA COMPLETE	0	0	0		15-Jan-20																								
Tyson's Scope																														
Mechanical/Piping																														
CA3-02210	A3 - OH Process Piping	100	0	100	21-Feb-20	13-Jul-20																								
CA3-02250	A3 - Rehigh/HAC Ductwork	90	0	90	20-Mar-20	27-Jul-20																								
CA3-04510	A3 - Compressed Air Equipment/Piping	92	0	92	21-Feb-20	30-Jun-20																								
CA3-04610	A3 - Chilled Water Equipment/Piping	140	0	140	21-Feb-20	07-Sep-20																								
CA3-04620	A3 - Cooling Tower/Piping on Roof	120	0	120	21-Feb-20	10-Aug-20																								
CA3-04710	A3 - Boiler Equipment/Piping/Ductwork	116	0	116	21-Feb-20	04-Aug-20																								
TRT-3r1 12 of 13 218068																														
PROJECT TYSON HT Overall Schedule																														
Start Date : 15-Aug-18 Data Date : 20-Mar-19 Run Date : 21-Mar-19																														
Actual Remaining Critical Milestone																														
Gray																														

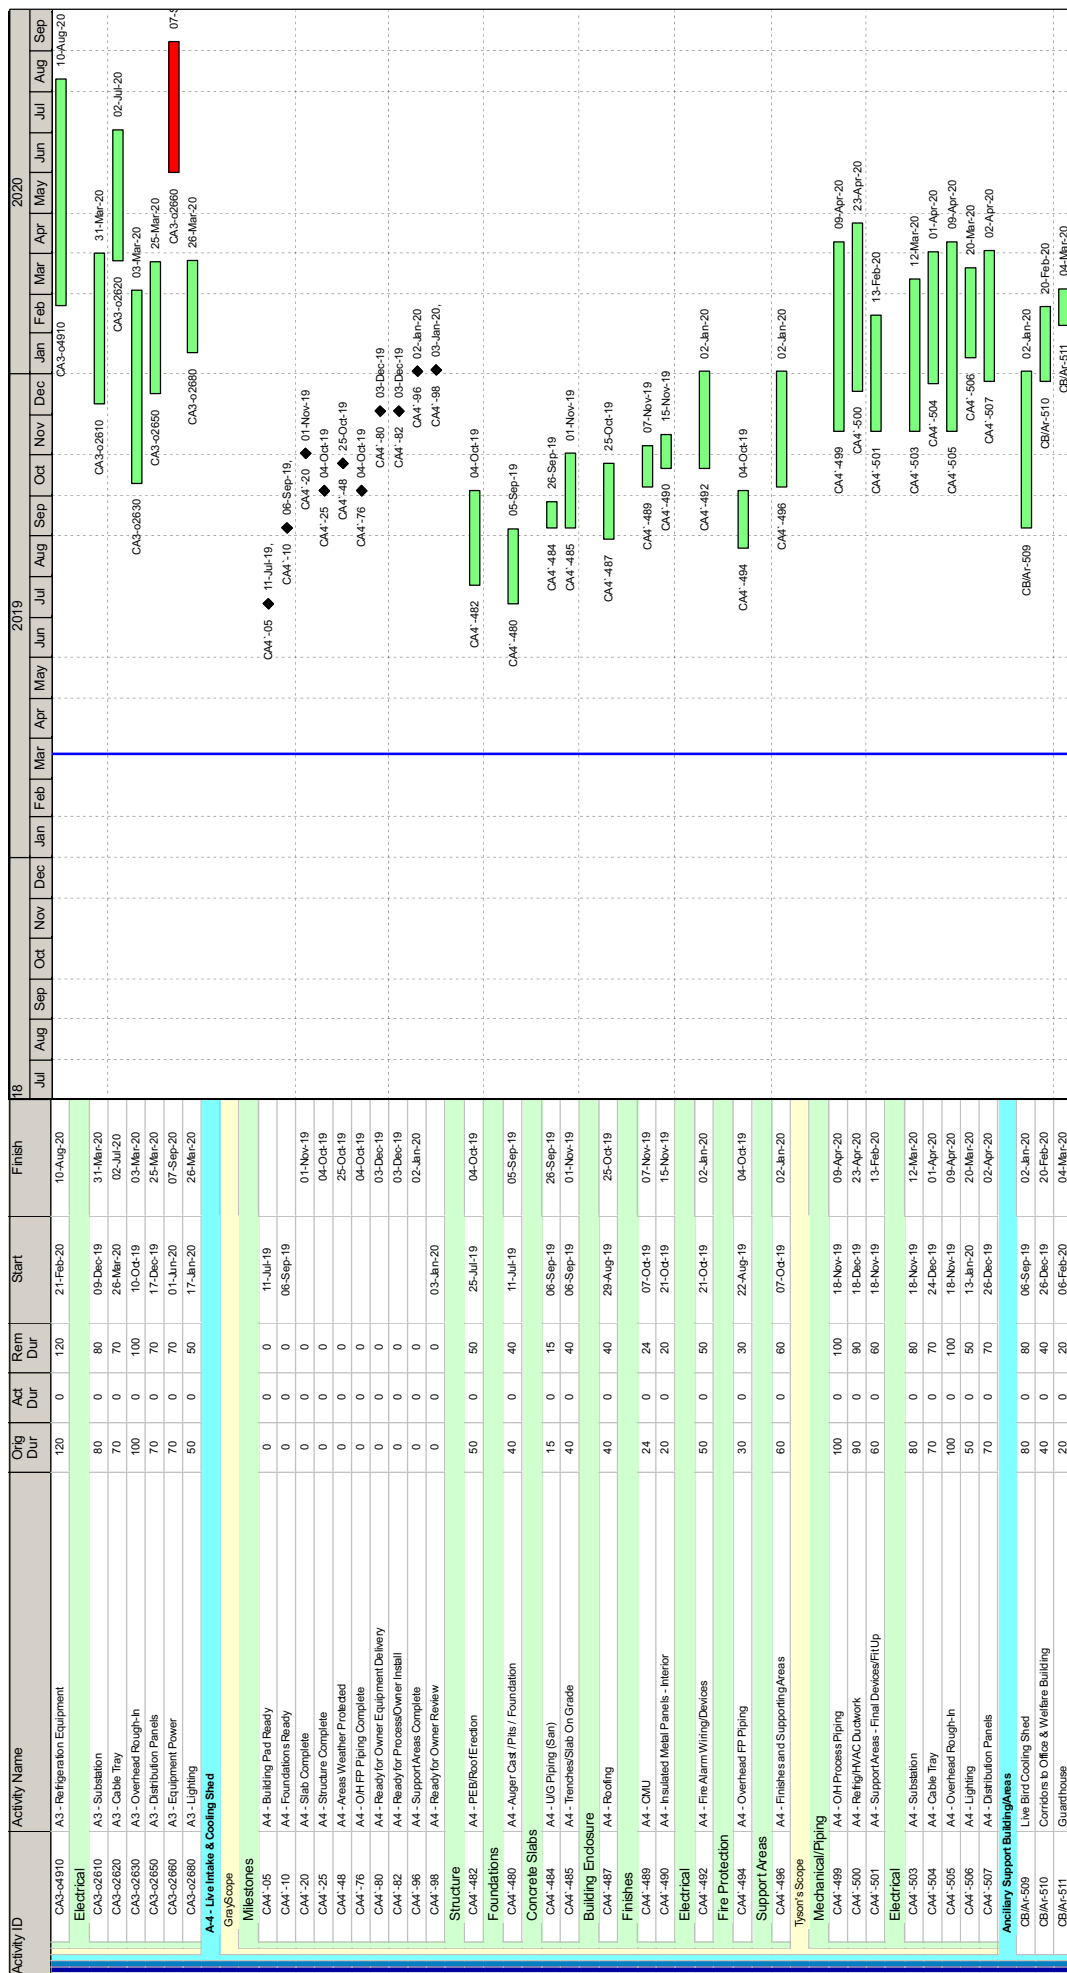

PROJECT TYSON HT  
Overall Schedule

Start Date : 15-Aug-18  
Data Date : 20-Mar-19  
Run Date : 21-Mar-19

Actual  
Remaining

Critical  
Milestone

TRT-3r1  
13 of 13  
218068





Thank you,  
Matt

**Matthew Cecil**

Project Manager



Gray  
10 Quality Street  
Lexington, KY 40507-1450  
Telephone: 859-281-9338  
Mobile: 859-358-4017  
Fax: 859-252-5300  
[mcecil@gray.com](mailto:mcecil@gray.com)  
[www.gray.com](http://www.gray.com)

Connect with us:



This e-mail, and any documents, files or previous e-mail messages attached to it may contain confidential, privileged or proprietary information. If you have received this communication in error, please contact the sender and destroy all copies of this email.
